Temporary Seeding Specifications

Seeding Dates	Species	Lb. / 1000sqft	Per Acre
March 1 to August 15	Oats Tall Fescue Annual Ryegrass Perennial Ryegrass Tall Fescue Annual Ryegrass	3 1 1 1 1 1	4 bushel 40 lb. 40 lb. 40 lb. 40 lb. 40 lb.
August 16 to November 1	Rye Tall Fescue Annual Ryegrass Wheat Tall Fescue Annual Ryegrass Perennial Ryegrass Tall Fescue Annual Ryegrass	1 1 1 1 1 1 1 1 1	2 bushel 40 lb. 40 lb. 40 lb. 40 lb. 40 lb. 40 lb. 40 lb. 40 lb.
November 1 to Spring Seeding	Use mulch only, sodding practices or dormant seeding		

Note: other approved seed species may be substituted.

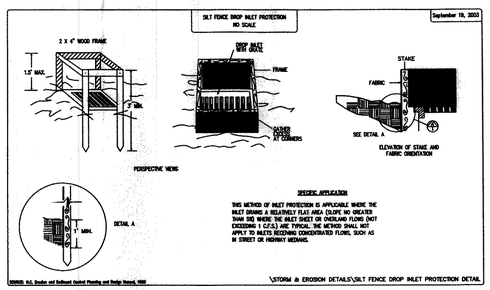

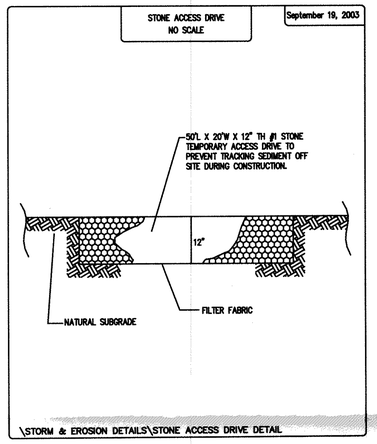

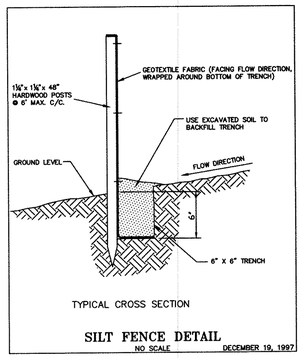

2 WORKING DAYS
BEFORE YOU DIG
CALL TOLL FREE 800-362-2764
OHIO UTILITIES PROTECTION SERVICE
NON-MEMBERS MUST BE CALLED DIRECT

EXISTING UNDERGROUND UTILITIES NOTE:
THE SIZE AND LOCATION, BOTH HORIZONTAL AND VERTICAL OF THE UNDERGROUND UTILITIES SHOWN HEREON, HAVE BEEN OBTAINED BY A SEARCH OF AVAILABLE RECORDS. VERIFICATION BY FIELD OBSERVATION HAS BEEN CONDUCTED WHERE PRACTICAL. HOWEVER, POLARIS ENGINEERING & SURVEYING, INC. DOES NOT GUARANTEE THE COMPLETENESS NOR ACCURACY THEREOF.

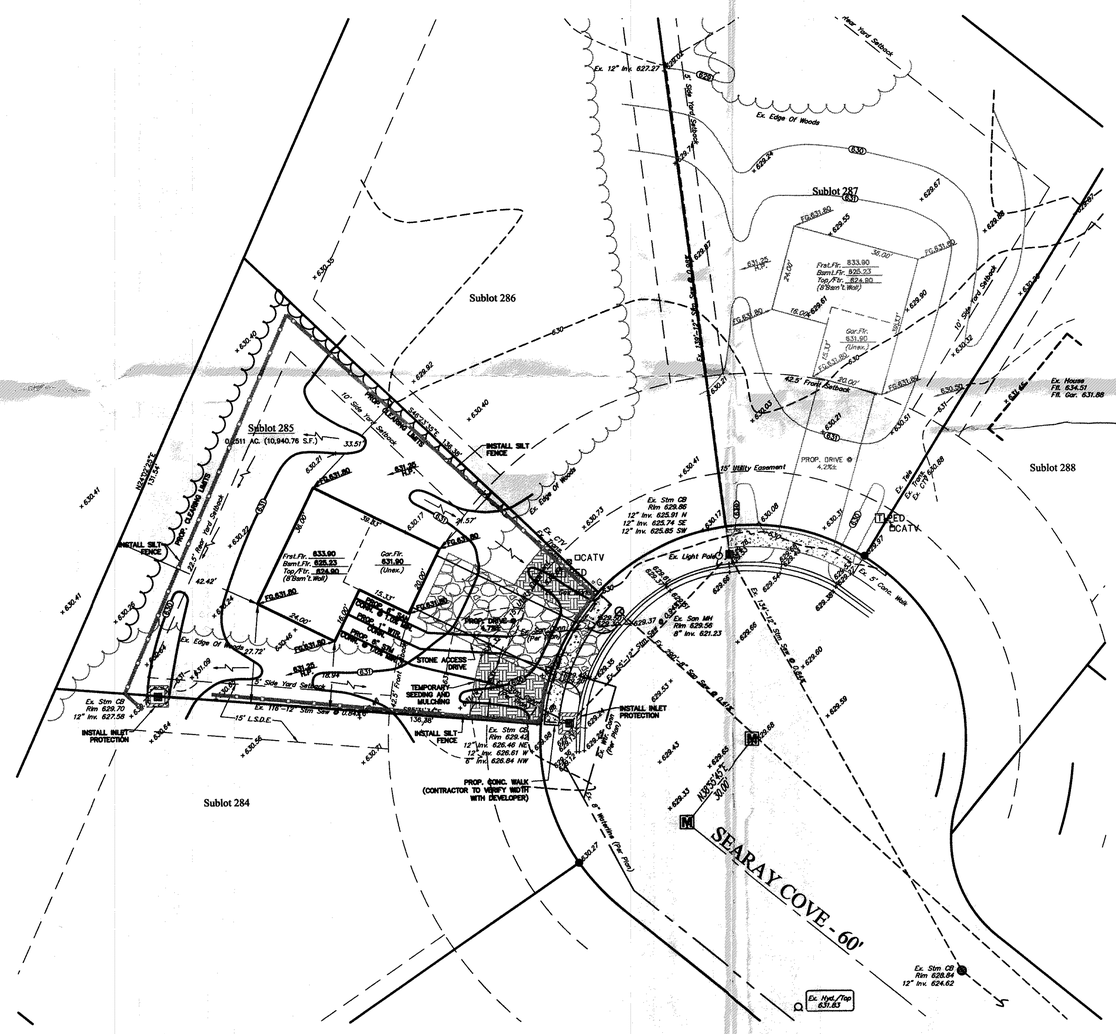



Elevations Used To Establish Floor Elevations:
- Gar.Flr.+10"=Top/Wall
- Top/Wall+12.0"(1.0')=Frst.Flr.
- Top Wall-8'-0"=Top/Flr.
- Top/Flr.+4"(0.33')=Bsmt.Flr.

ESTIMATED IMPERVIOUS AREA
HOUSE: 0.03Ac.
DRIVE: 0.02Ac.
TOTAL: 0.05Ac.

NOTE:
- Contractor To Verify Location & Depth Of Laterals;
- See Architect Plans For Complete House Dimensions;
- Drive Apron To Be 6" Thick Concrete With 3 Foot Flares;
- Sidewalk To Be ODOT-608, 4" Thick(6" @ Driveway) With 3" Gravel Or Sandbase.
- Sump Pump To Discharge To Proposed Storm Connection.
- Proposed Downspouts To Outlet To Splashblocks.
- Splashblocks To Be Directed Toward The Front And Rear Of The Lot (Not Toward Adjacent Properties)
- See Architect Plans For Downspout Locations.

APPROVED
20110224 12-21-11
PERMIT # DATE
Painesville Township Zoning Inspector

Erosion and Sediment Control Schedule

Ingress-Egress
A stone access drive complete with under lying geo-textile fabric (20 feet wide and 50 feet long) for ingress and egress at the site shall be installed. This drive shall be the only entrance and exit to the site.

Silt Fence
All silt fence shall be installed prior to any earthwork activities at the site in the locations shown on the site plan as well as along the front of any lot that slopes towards the street.

Temporary Seeding
Disturbed areas of the site that are to remain idle for more than twnty-one (21) days shall be properly seeded and straw mulched within seven (7) days of completion of initial grading.
Temporary seeding and mulching of a thirty (30) foot strip of the entire front of the lot shall be maintained on the site once initial grading is complete.

Stabilization of critical areas within fifty (50) feet of any stream or wetland shall be complete within two (2) days of the disturbance if the site is to remain inactive for longer than fourteen (14) days.

Mulching
Straw-mulch shall be applied at a rate of 1 bale per every ten (10) feet of curb, at a width of thirty (30) feet of the entire length of the lot. Wood chips may also be used but must be spread at a minimum depth of four inches over the thirty-foot width and must be accompanied by a properly installed silt fence.

Maintenance
Erosion and sediment controls shall be inspected every seven (7) days or within 24 hours of a 0.5" or greater rainfall event. Necessary repairs shall be made at this time.

Note:
All erosion and sediment control specifications, applications, and timetables are based on the descriptions and standards of The Ohio Department of Natural Resources "Rainwater and Land Development Manual" and can be found in the Lake County Erosion and Sediment Control Rules as adopted December 21, 1999

The specified erosion and sediment control standards are general guidelines and shall not limit the right of the county to impose, at any time, additional, more stringent requirements. Nor shall the standards limit the right of the county to waive, in writing, individual requirements.

I, THE UNDERSIGNED, HEREBY CERTIFY THAT THIS TOPOGRAPHY, INDICATED BY 6", 1', OR 2' CONTOURS, AND ELEVATIONS SHOWN HEREON, REPRESENT AN ACTUAL FIELD SURVEY MADE BY ME ON THE 21st DAY OF NOVEMBER, 2011, AND THAT THE ELEVATIONS WERE TAKEN AT APPROPRIATE INTERVALS AND THAT AS OF THAT DATE, THEY EXISTED AS INDICATED HEREON.

Charles W. Szucs, P.S.8240

STATE OF OHIO CHARLES W. SZUCS S-8240 REGISTERED PROFESSIONAL SURVEYOR

Site & Grade Hse. 12-2-11

polaris Engineering & Surveying

POLARIS ENGINEERING & SURVEYING, INC.
34600 CHARDON ROAD - SUITE D
WILLOUGHBY HILLS, OHIO 44094
(440) 944-4433 (440) 944-3722 (Fax)
www.polaris-es.com

DESIGN CERTIFICATION

THIS PLAN WAS PREPARED BY ME, AND IS CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF.

NAME 12/2/11 DATE

BENCHMARK:

B.M. = T.B.M Set On Top Of Hydrant
Located As Noted
Elevation 631.83

STATE OF OHIO CHARLES W. SZUCS S-8240 REGISTERED PROFESSIONAL SURVEYOR
STATE SEAL

"AS-BUILT" CERTIFICATION

I HEREBY CERTIFY THAT THE CIRCLED INFORMATION IS EXISTING AS OBTAINED ON THE SITE _____ AND IS CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF.

NAME DATE

Prepared For:
Canterbury Homes, Inc.
Ron Klein/Marc Kaplovitz
29899 Smithfield
Orange, Ohio 44022

SUBLOT 285

Lake Erie Shores Ph.4A

(Volume 50 Page 33)
Painesville Twp. - Lake County - Ohio

CONTRACT No. 09084
DATE: 12/2/11
SCALE: HOR. 1"=20'
VERT.
FILENAME: Sublot285.dwg

Stormwater Management Plan
Approved as shown and/or noted
JAMES R. GILLE, P.E.
County Drainage Engineer
By J.S. Date 12/23/11
